

Medivac Crew Facilities 2nd Quarter Task Name Duration Start Finish 3rd Quarter Mar May Jun Aug Apr Jul Board Approval for Project 3/24 3/24 Thu 3/24/11 Thu 3/24/11 1 day 3/25 Site & Structural Design Development 10 days Fri 3/25/11 Thu 4/7/11 4/7 3/25 3/31 Write RFP for Modular Building 5 days Fri 3/25/11 Thu 3/31/11 3/25 TDPUD Electrical Design 4/21 20 days Fri 3/25/11 Thu 4/21/11 RFP Response Process 4/1 4/21 15 days Fri 4/1/11 Thu 4/21/11 4/14 Submit for Special Use Permit 5 days Fri 4/8/11 4/8 Thu 4/14/11 Special Use Permit Review Process Fri 4/15/11 Thu 7/14/11 4/15 7/14 65 days Modular Selection Process 10 days Fri 4/22/11 Thu 5/5/11 4/22 5/5 Modular Building Engineering & Drawings Fri 7/15/11 Thu 8/4/11 7/15 15 days 8/4 7/15 Civil & Structural Construction Documents 8/4 15 days Fri 7/15/11 Thu 8/4/11 Building Permit Application 1 day Fri 8/5/11 Fri 8/5/11 8/5 8/5 8/8 Sitework Informal Bid Process Mon 8/8/11 Fri 8/26/11 15 days 8/8 Building Permit Review Process 25 days Mon 8/8/11 Fri 9/9/11 Site Contract Paperwork 10 days Mon 8/29/11 Fri 9/9/11 Modular Building Offsite Construction 25 days Mon 9/12/11 Fri 10/14/11 Site Construction 30 days Mon 9/12/11 Fri 10/21/11 Modular Building Placement & Hookup 5 days Mon 10/24/11 Fri 10/28/11 Modular Building Inspection and Certificate of Occupancy 5 days Mon 10/31/11 Fri 11/4/11



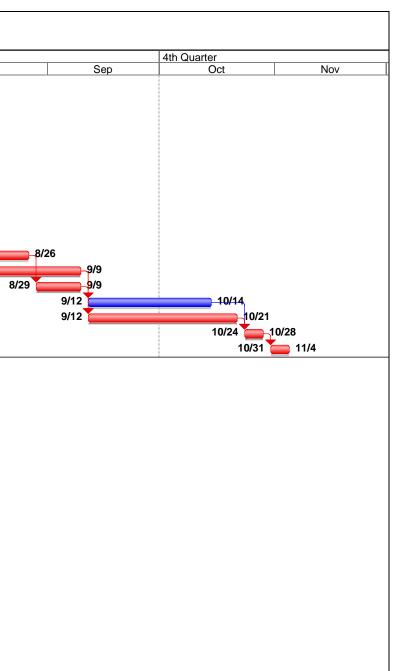

oup By Summary	
adline	$\hat{\nabla}$
